

	DAILY REPORT		
	HARI/ TANGGAL	Rabu, 29 Januari 2025	
	PM PIC	Abdul Mudzakir M Ramdan Suprayogi	

							Title Project	PEMBANGUNAN PIPA TRANSMISI GAS BUMI CIREBON-SEMARANG TAHAP 2 RUAS BATANG – CIREBON – KANDANG HAUR TIMUR)
MANPOWER	QTY				Total Manpowe	Total Hours		
	TLB	Open Cut	Rojok	Katrek				
PM	1				1		No. Kontrak	SO-000011-CSM-I-2025
SPV	1				1			
QA/QC	1				1		No. Doct	PMRK-PRD-DLY-007
Tukang	4				4			

CUACA	Normal	07.00	09.00	11.00	13.00	15.00	17.00	Over Time	18.00	20.00	22.00
Hujan Gerimis				√							
Hujan Sedang			√	√		√	√		√		
Hujan Lebat		√	√		√						
Mendung				√			√				
Cerah											

No	EQUIPMENT	QTY	HOURSE
1	Cangkul	3	
2	Plancong	1	
3			
4			
5			
6			
7			
8			
9			
10			

No	KENDALA	SOLUSI
1	Menunggu Pekerjaan Pipa	
2		
3		
4		
5		
6		
7		

JOB DESCRIPTION										
No	ITEM	QTY Plan	unit	QTY Prev	unit	QTY Today	Unit	QTY Comm	Unit	Per %
1	Pekerjaan ROW Pertagas									
	- Open cut manual	18.000	meter		meter		meter	0,0	meter	0,00%
	- Laying FO cable (40000 meter)	40.000	meter		meter		meter	0,0	meter	0,00%
	- Boring manual crossing	2.000	meter		meter		meter	0,0	meter	0,00%
	- Pembuatan box Control	5	box		box		box	0,0	box	0,00%
	- Enclosure	10	unit		unit		unit	0,0	unit	0,00%
	- Splicing FO < 0,3 dB	120	core		core		core	0,0	core	0,00%
	- OTDR	40	km		km		km	0,0	km	0,00%
2	Pekerjaan BPJN (Jalan Nasional)									
	- TLB (Subduct Bareng pipeline)	27.000	meter	100	meter	25,0	meter	125,0	meter	0,46%
	- Pengadaan subduct (Vinillon)	37.000	meter		meter		meter	0,0	meter	0,00%
	- Laying FO cable (40000 meter)	76.000	meter		meter		meter	0,0	meter	0,00%
	- Boring manual (Estimasi)	8.200	meter		meter		meter	0,0	meter	0,00%
	- Boring manual crossing	1.800	meter		meter		meter	0,0	meter	0,00%
	- Pembuatan box Control	9	box		box		box	0,0	box	0,00%
	- Enclosure	19	unit		unit		unit	0,0	unit	0,00%
	- Splicing FO < 0,3 dB	222	core		core		core	0,0	core	0,00%
	- OTDR	74	km		km		km	0,0	km	0,00%
3	SAT	1	lot		lot		lot	0,0	lot	0,00%

	DAILY REPORT		
	HARI/ TANGGAL PM PIC	Rabu, 29 Januari 2025 Abdul Muzakir M Ramdan Suprayogi	

Dokumentasi :



Penanaman Subduct KP 276+500



Penanaman Subduct KP 276+500



Penanaman Subduct KP 276+500



Penanaman Subduct KP 276+500




Penimbunan Subduct KP 276+500



Penanaman Subduct KP 276+500



Penanaman Subduct KP 276+500

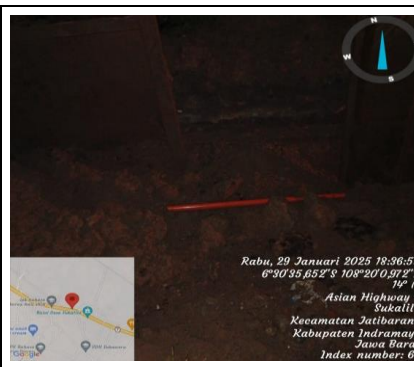

Penanaman Subduct KP 276+500



Penanaman Subduct KP 276+500

Remark :

--

Dibuat :

Disetujui :

PT. Pasopati Rekadaya	KSO Timas-Pratiwi
	
Ramdan Suprayogi	
