

	DAILY REPORT		
	HARI/ TANGGAL	Kamis, 20 Februari 2025	
	PM	Abdul Mudzakir M	
	PIC	Ramdan Suprayogi	
	LOKASI	KP.280+800	
No. Contract	Title Project		No. Document
SO-000011-CSM-I-2025	PEMBANGUNAN PIPA TRANSMISI GAS BUMI CIREBON-SEMARANG TAHAP 2 RUAS BATANG – CIREBON – KANDANG HAUR TIMUR)		PMRK-CSMII-DLY-PRD-009

No.	MANPOWER	QTY			Total Hours
		Qty Prev	Qty Today	Qty Cum	
1	Project Manager	1	1	2	16
2	Supervisor	1	1	2	16
3	QA/QC	1	1	2	16
4	HSE Officer	1	1	2	16
5	Paramedic	1	1	2	16
6	Foreman	2	2	4	32
7	Helper	19	19	38	304
8	Flagman	2	2	4	32
9				0	0
10				0	0
Sum		28	28	56	448

CUACA	Normal	07.00	09.00	11.00	13.00	15.00	17.00	Over Time	18.00	20.00	22.00
Hujan Gerimis											
Hujan Sedang											
Hujan Lebat											
Mendung											
Cerah		√	√	√	√	√	√				

No	EQUIPMENT	QTY	HOURSE
1	Rambu Ukur	1	
2	Set Alat Boring Manual	8	
3	Cangkul	18	
4	blencong	18	
5	Linggis	8	
6	Meteran	1	
7	Golok	8	
8	Ember	16	
9			
10			

No	KENDALA	SOLUSI
1		
2		
3		
4		
5		

JOB DESCRIPTION									
No	ITEM	QTY Plan	unit	QTY Prev	Prev %	QTY Today	Today %	QTY Cumm	Cumm %
1	Pekerjaan ROW Pertagas								
	- Open cut manual	18.000	meter		0,00%		0,00%	0,0	0,00%
	- Laying FO cable (40000 meter)	40.000	meter		0,00%		0,00%	0,0	0,00%
	- Haspel 1,2	8.000							
	- Haspel 3,4	8.000							
	- Haspel 5,6	8.000							
	- Haspel 7,8	8.000							
	- Haspel 9,10	8.000							
	- Boring manual crossing	2.000	meter		0,00%		0,00%	0,0	0,00%
	- Pembuatan box Control	5	box		0,00%		0,00%	0,0	0,00%
2	Pekerjaan BPJN (Jalan Nasional)								
	- TLB (Subduct Bareng pipeline)	27.000	meter	834,00	0,00%	294,00	1,09%	1128,0	1,09%
	- Laying FO cable (40000 meter)	76.000	meter		0,00%		0,00%	0,0	0,00%
	- Haspel 11,12	8.000							


	DAILY REPORT		
	HARI/ TANGGAL	Kamis, 20 Februari 2025	
	PM	Abdul Mudzakir M	
	PIC	Ramdan Suprayogi	
	LOKASI	KP.280+800	

JOB DESCRIPTION									
No	ITEM	QTY Plan	unit	QTY Prev	Prev %	QTY Today	Today %	QTY Cumm	Cumm %
	- Haspel 13,14	8.000							
	- Haspel 15,16	8.000							
	- Haspel 17,18	8.000							
	- Haspel 19,20	8.000							
	- Haspel 21,22	8.000							
	- Haspel 23,24	8.000							
	- Haspel 25,26	8.000							
	- Haspel 27,28	8.000							
	- Haspel 29	4.000							
	- Boring manual (Estimasi)	8.200	meter	834,00	0,00%	294,00	3,59%	1128,0	3,59%
	- Boring manual crossing	1.800	meter		0,00%		0,00%	0,0	0,00%
	- Pembuatan box Control	9	box		0,00%		0,00%	0,0	0,00%
3	SAT	1	lot		0,00%		0,00%	0,0	0,00%

Dokumentasi :



Laying Subduct

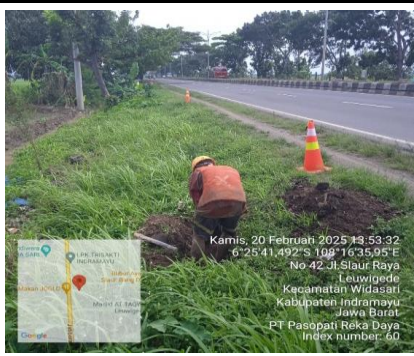

Laying Subduct



Laying Subduct



Laying Subduct



Laying Subduct



Laying Subduct

Remark :

Dibuat :

PT. Pasopati Rekadaya

Disetujui :

KSO Timas-Pratiwi
